

16 September 2022

## To all residents of Golden Mile House

Dear Resident,

### Re: Dismantling of scaffold at Golden Mile House

My we take this opportunity to thank you for your continued patience regarding the works.

The cladding remediation work at Golden Mile House is moving towards completion. Please see the diagram on the following page, explaining how the scaffold will be dismantled from the building, including the dates which this is forecast to take place

The dismantling of the scaffold is due to begin on Tuesday 20<sup>th</sup> September 2022 and be completed by Saturday 5<sup>th</sup> November 2022.

The scaffold will be dismantled from the top floor down, elevation by elevation starting with eastern elevation (facing towards London) and then moving in an anti-clockwise direction around the building.

Please note that the above dates are subject to favourable weather conditions.


If you require any further clarification or have any questions about the works, please contact NewmanFrancis by writing to us at [gwq@newmanfrancis.org](mailto:gwq@newmanfrancis.org). You can also check our webpage to see the latest updates about the project – [www.newmanfrancis.org/gwq](http://www.newmanfrancis.org/gwq).

Yours faithfully



Jonathan Small  
Resident Liaison Service Manager

**Block 16 – Golden Mile House**  
Anticipated Striking sequence and programme

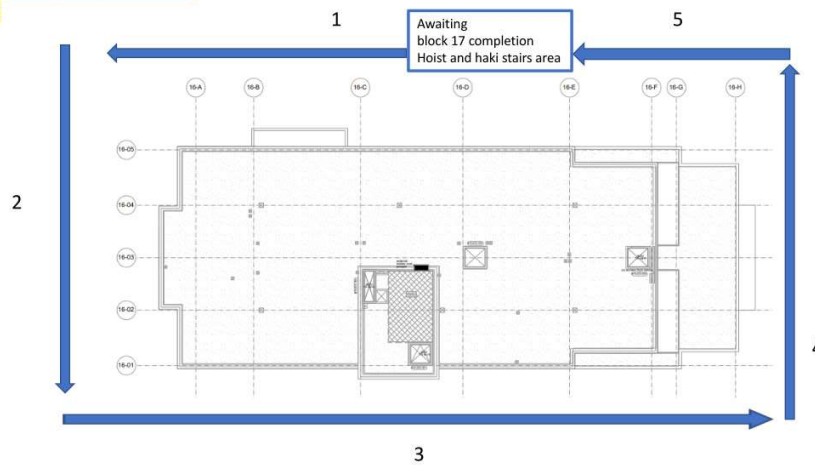

**Anticipated Striking Dates:**

- Level 6: 19-24/9
- Level 5: 26/9 – 1/10
- Level 4: 3-8/10
- Level 3: 10-15/10
- Level 2: 17 – 22/10
- Level 1: 24 – 29/10
- Level 0: 31/10 – 5/11

+ 2 weeks – weather and other delays
